



Crittenden Middle School & Theuerkauf Elementary School Electrical Upgrades

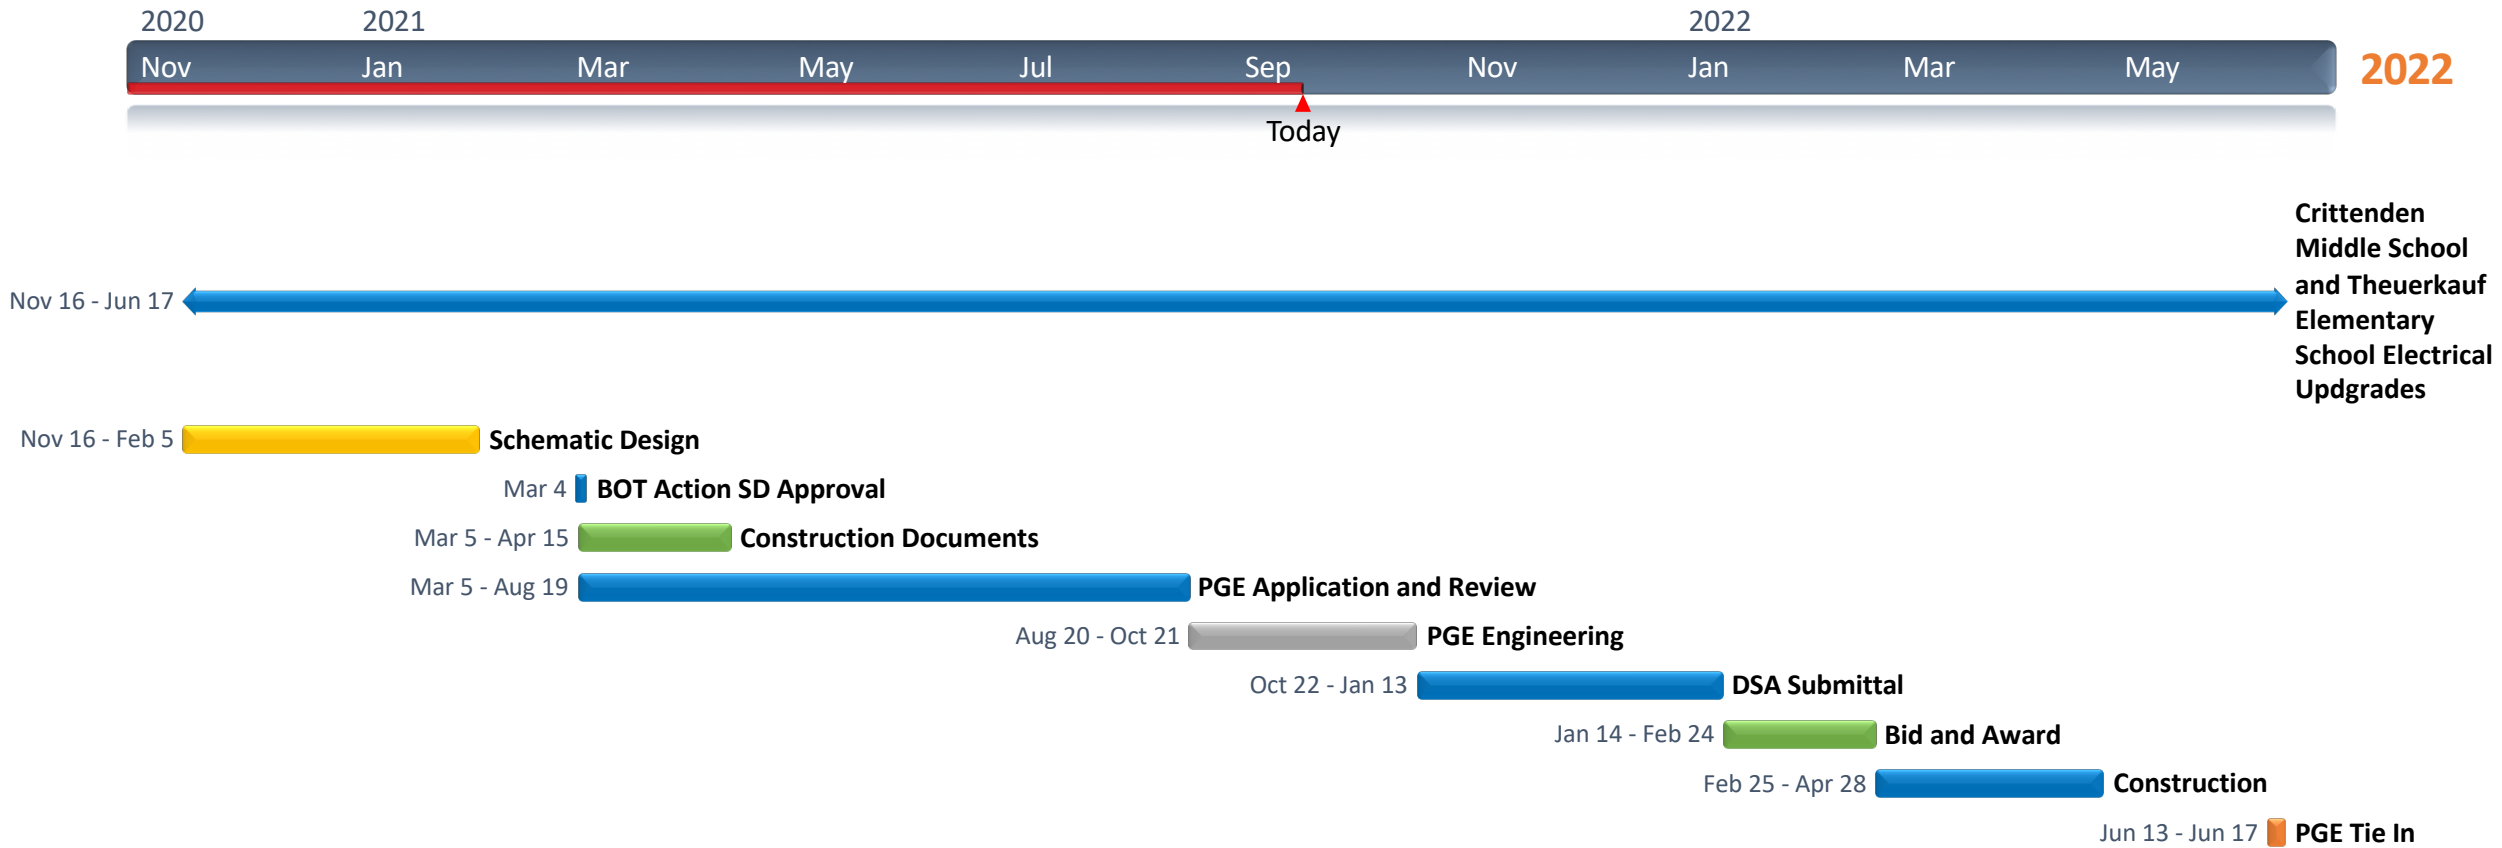

Imai Portable Project

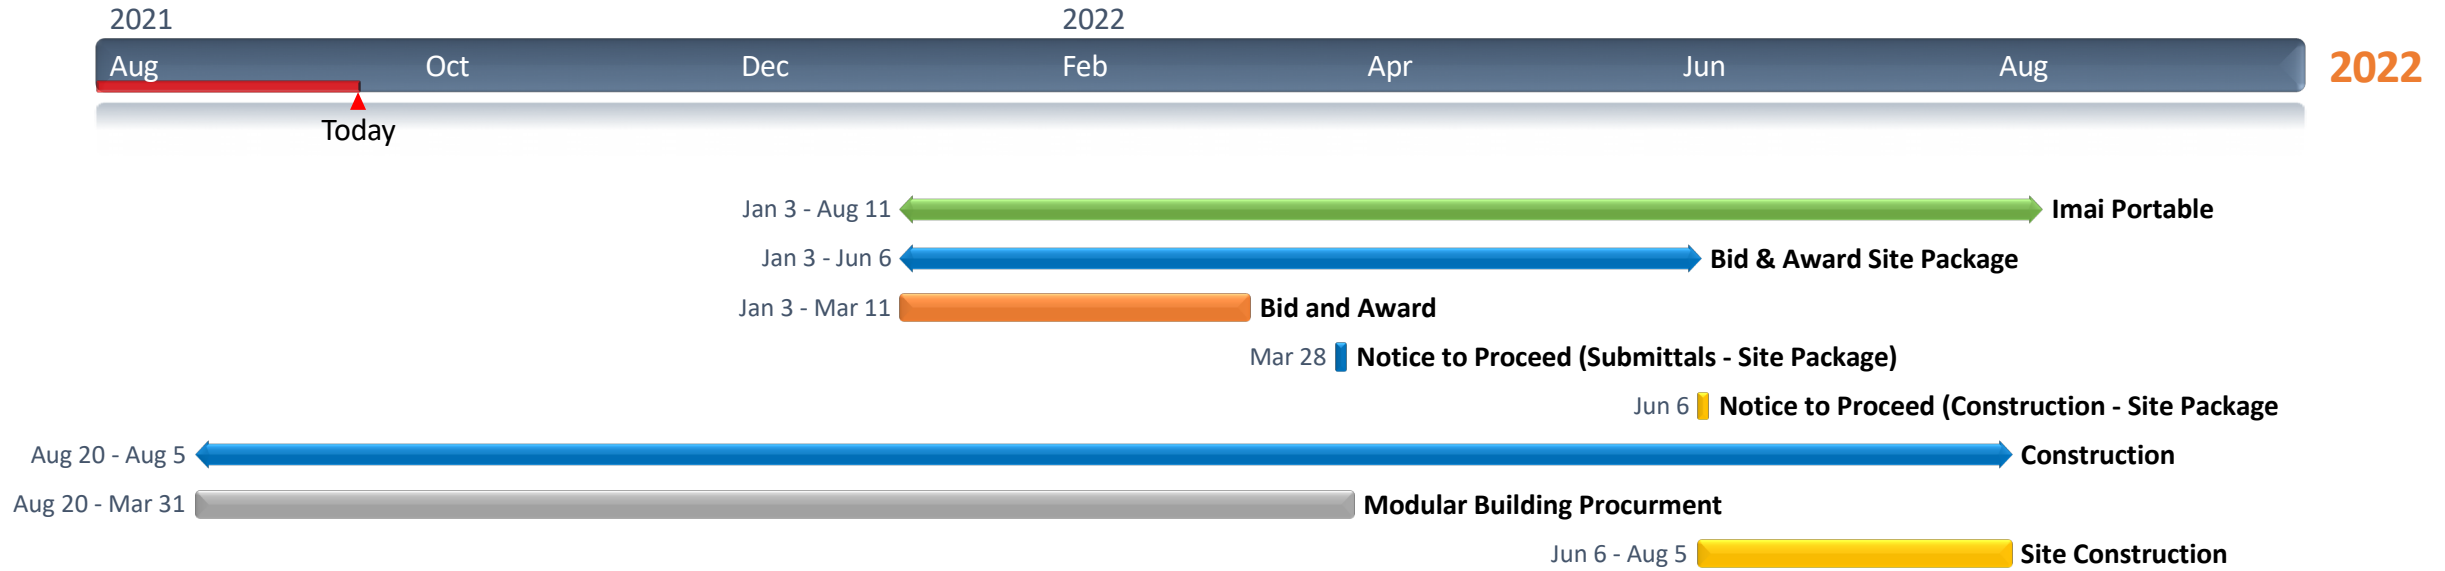

Landels New Building



2024

Nov 1 - May 10 ← Landels New Building →

Nov 1 **Update Calpeds**

Nov 2 - Nov 26 **Update Demographics**

Nov 29 - Dec 24 **BOT Action Project Approval**

Dec 27 - Feb 4 **Prepare Bridging Documents**

Feb 7 - Feb 18 **Issue RFP Design-Build Services**

Feb 21 - Apr 1 **Proposals Due**

Apr 4 - Apr 29 **Scoring and Award**

May 2 - Jan 6 **Prepare Construction Documents**

Jan 9 - Jun 9 **DSA Submittal and Review**

Jun 12 - Aug 11 **Demolition and Building Pad**

Jun 12 - Aug 11 **Temp Housing**

Aug 14 - May 10 **Construct New Building**

Jun 12 - Aug 4 **Remove Temp Camus**

Jun 12 - Aug 11 **Build New Parking/Drop Off**

Monta Loma Fields Renovation & Replacement



Jul 6 **Issue RFP for Architect/Landscape Archtiect**

Aug 4 **RFP's Due**

Aug 5 - Sep 15 **RFP Scoring and Interviews**

Sep 23 **Award of Archtectural Services Contract**

Sep 24 - Jan 27 **Programming**

Jan 28 - Apr 21 **Schematic Design**


Apr 22 - Jul 14 **Construction Documents**

Jul 15 - Sep 8 **DSA Reivew**

Sep 9 - Dec 1 **Lease-Leaseback Process**

May 1 - Sep 1 **Construction**

HVAC Replacement- DSA Review Required (Crittenden, Monta Loma & Theuerkauf)

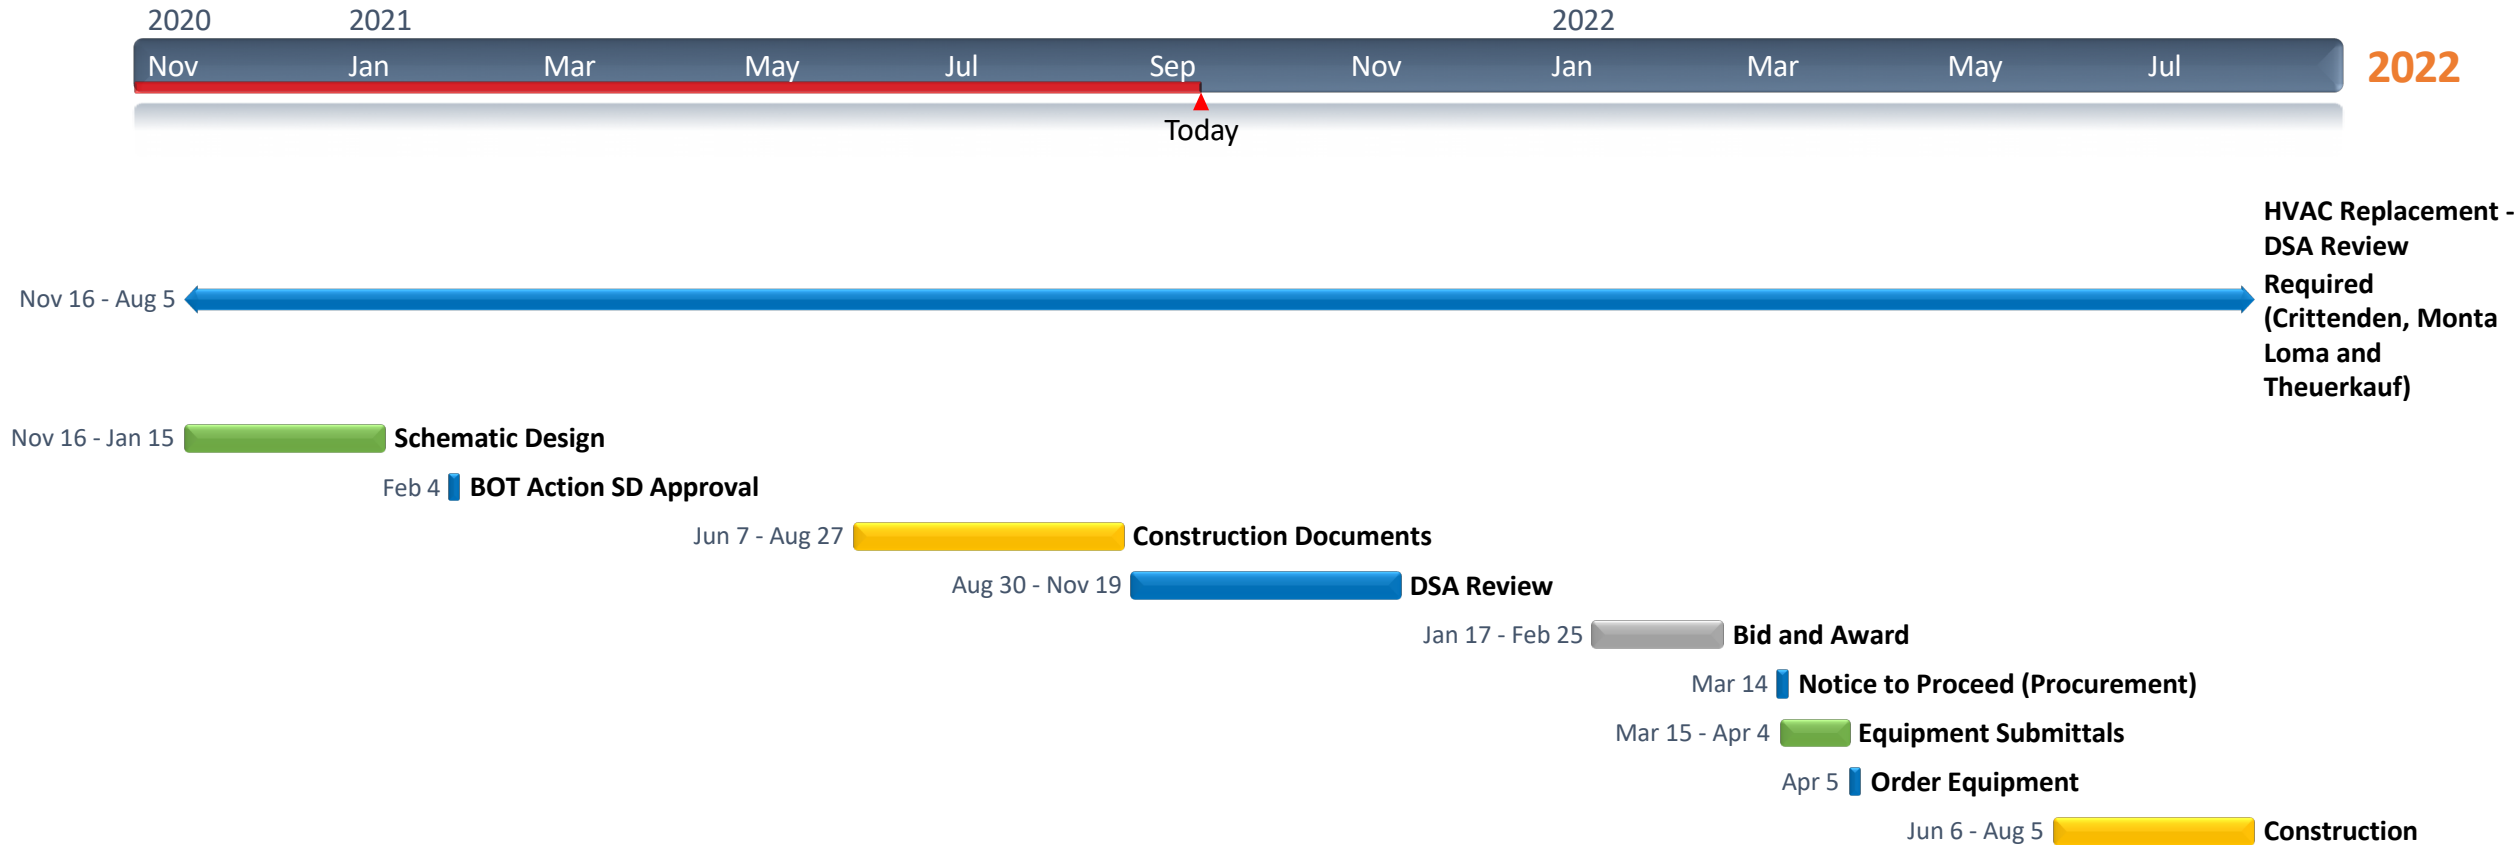

Outdoor Learning



Oct 4 - Aug 4 ← **Outdoor Learning** →

Oct 4 - Dec 24 **Programming**

Dec 27 - Feb 4 **Schematic Design**

Feb 10 **Board Action - Approve Schematic Design, Budget and Schedule**


Feb 11 - Apr 7 **Construction Documents**

Apr 8 - Jun 30 **DSA Review (Access Only)**



Jul 1 - Aug 18 **Bid & Award**

Jun 5 - Aug 4 **Construction**


Site Lighting

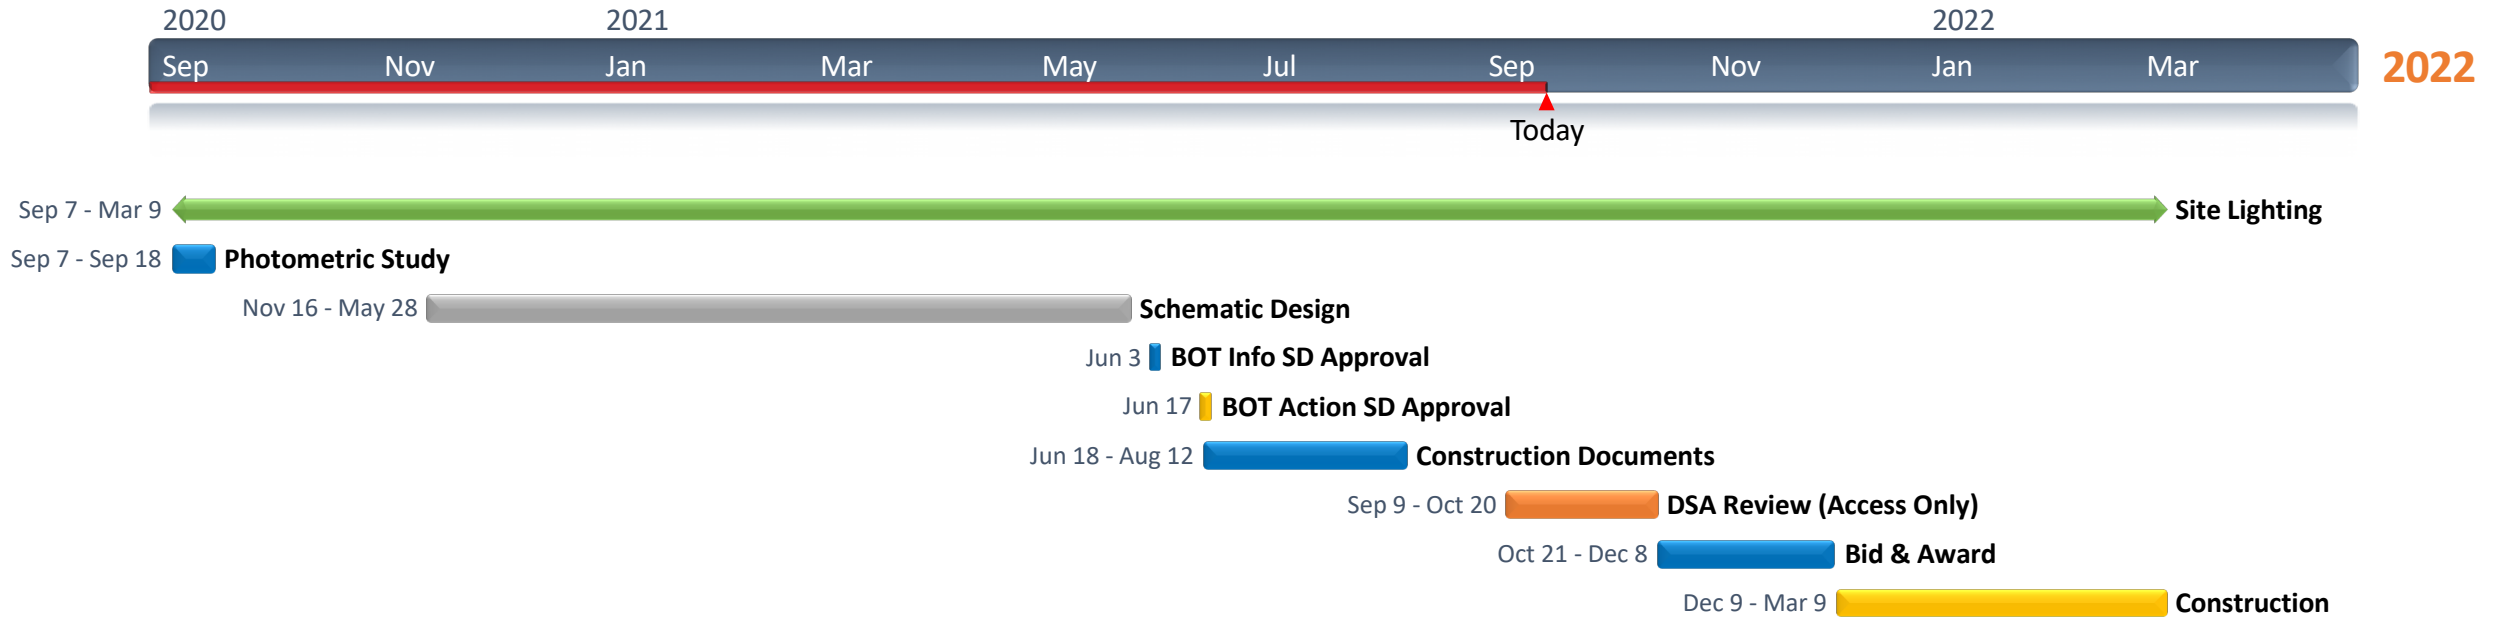

MVWSD Solar Project

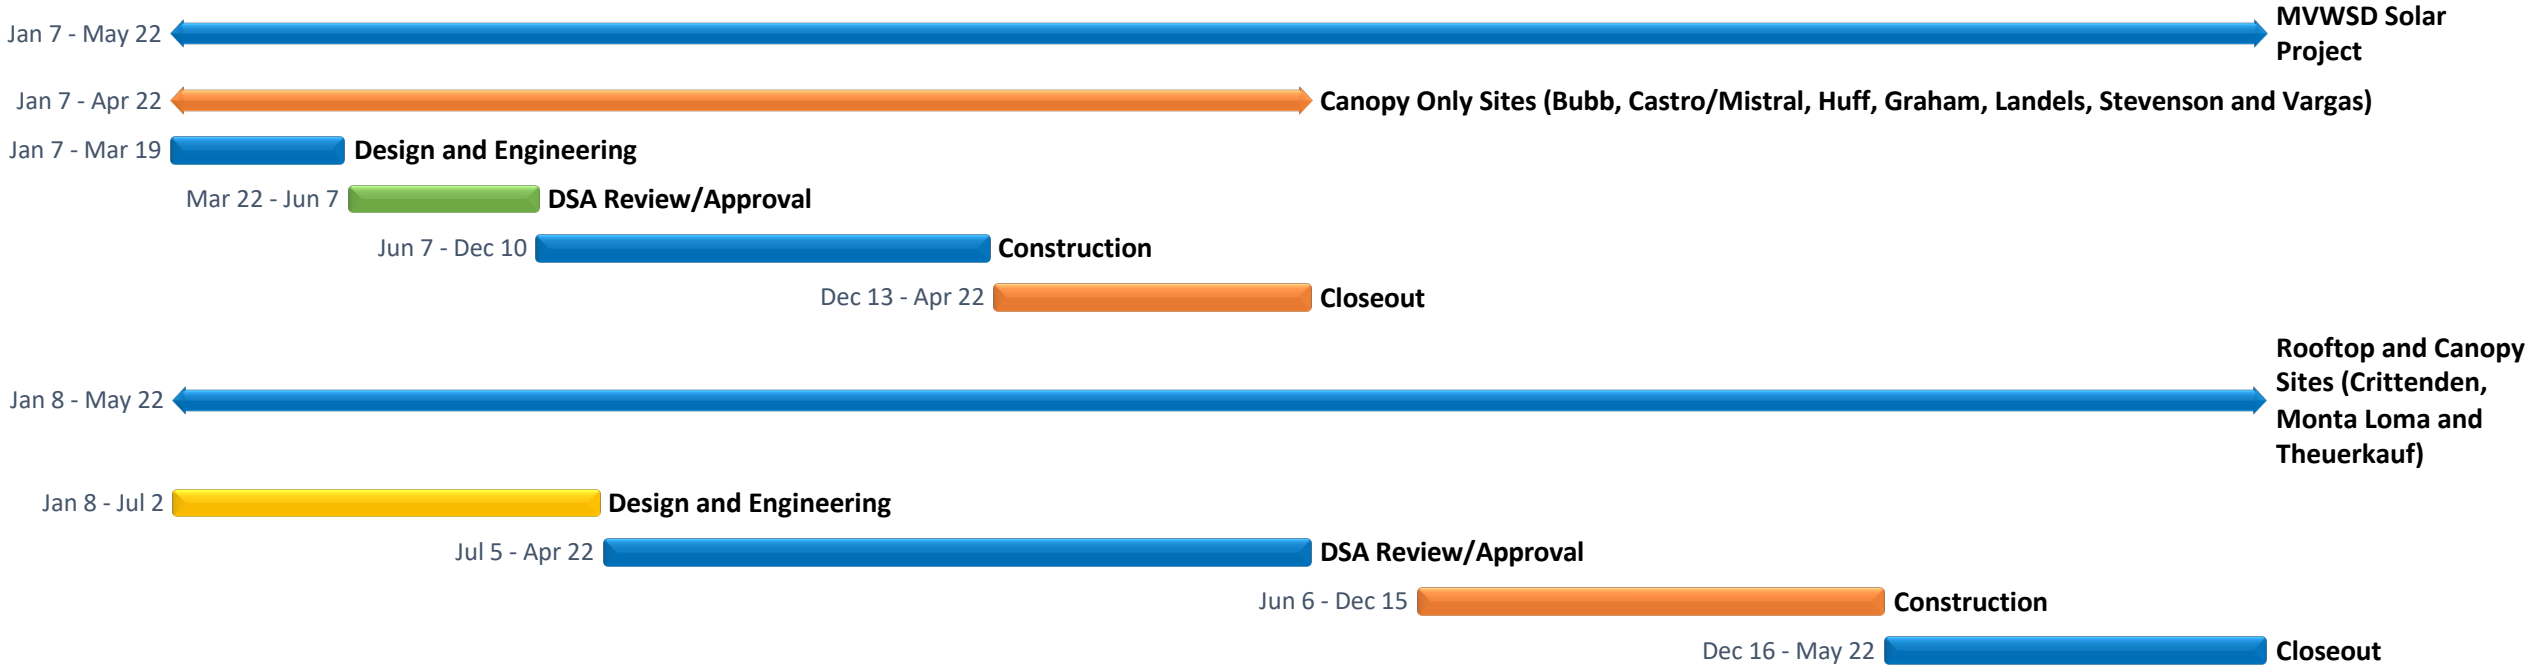

MVWSD Window Replacement Project (phase 1 pending board approval)

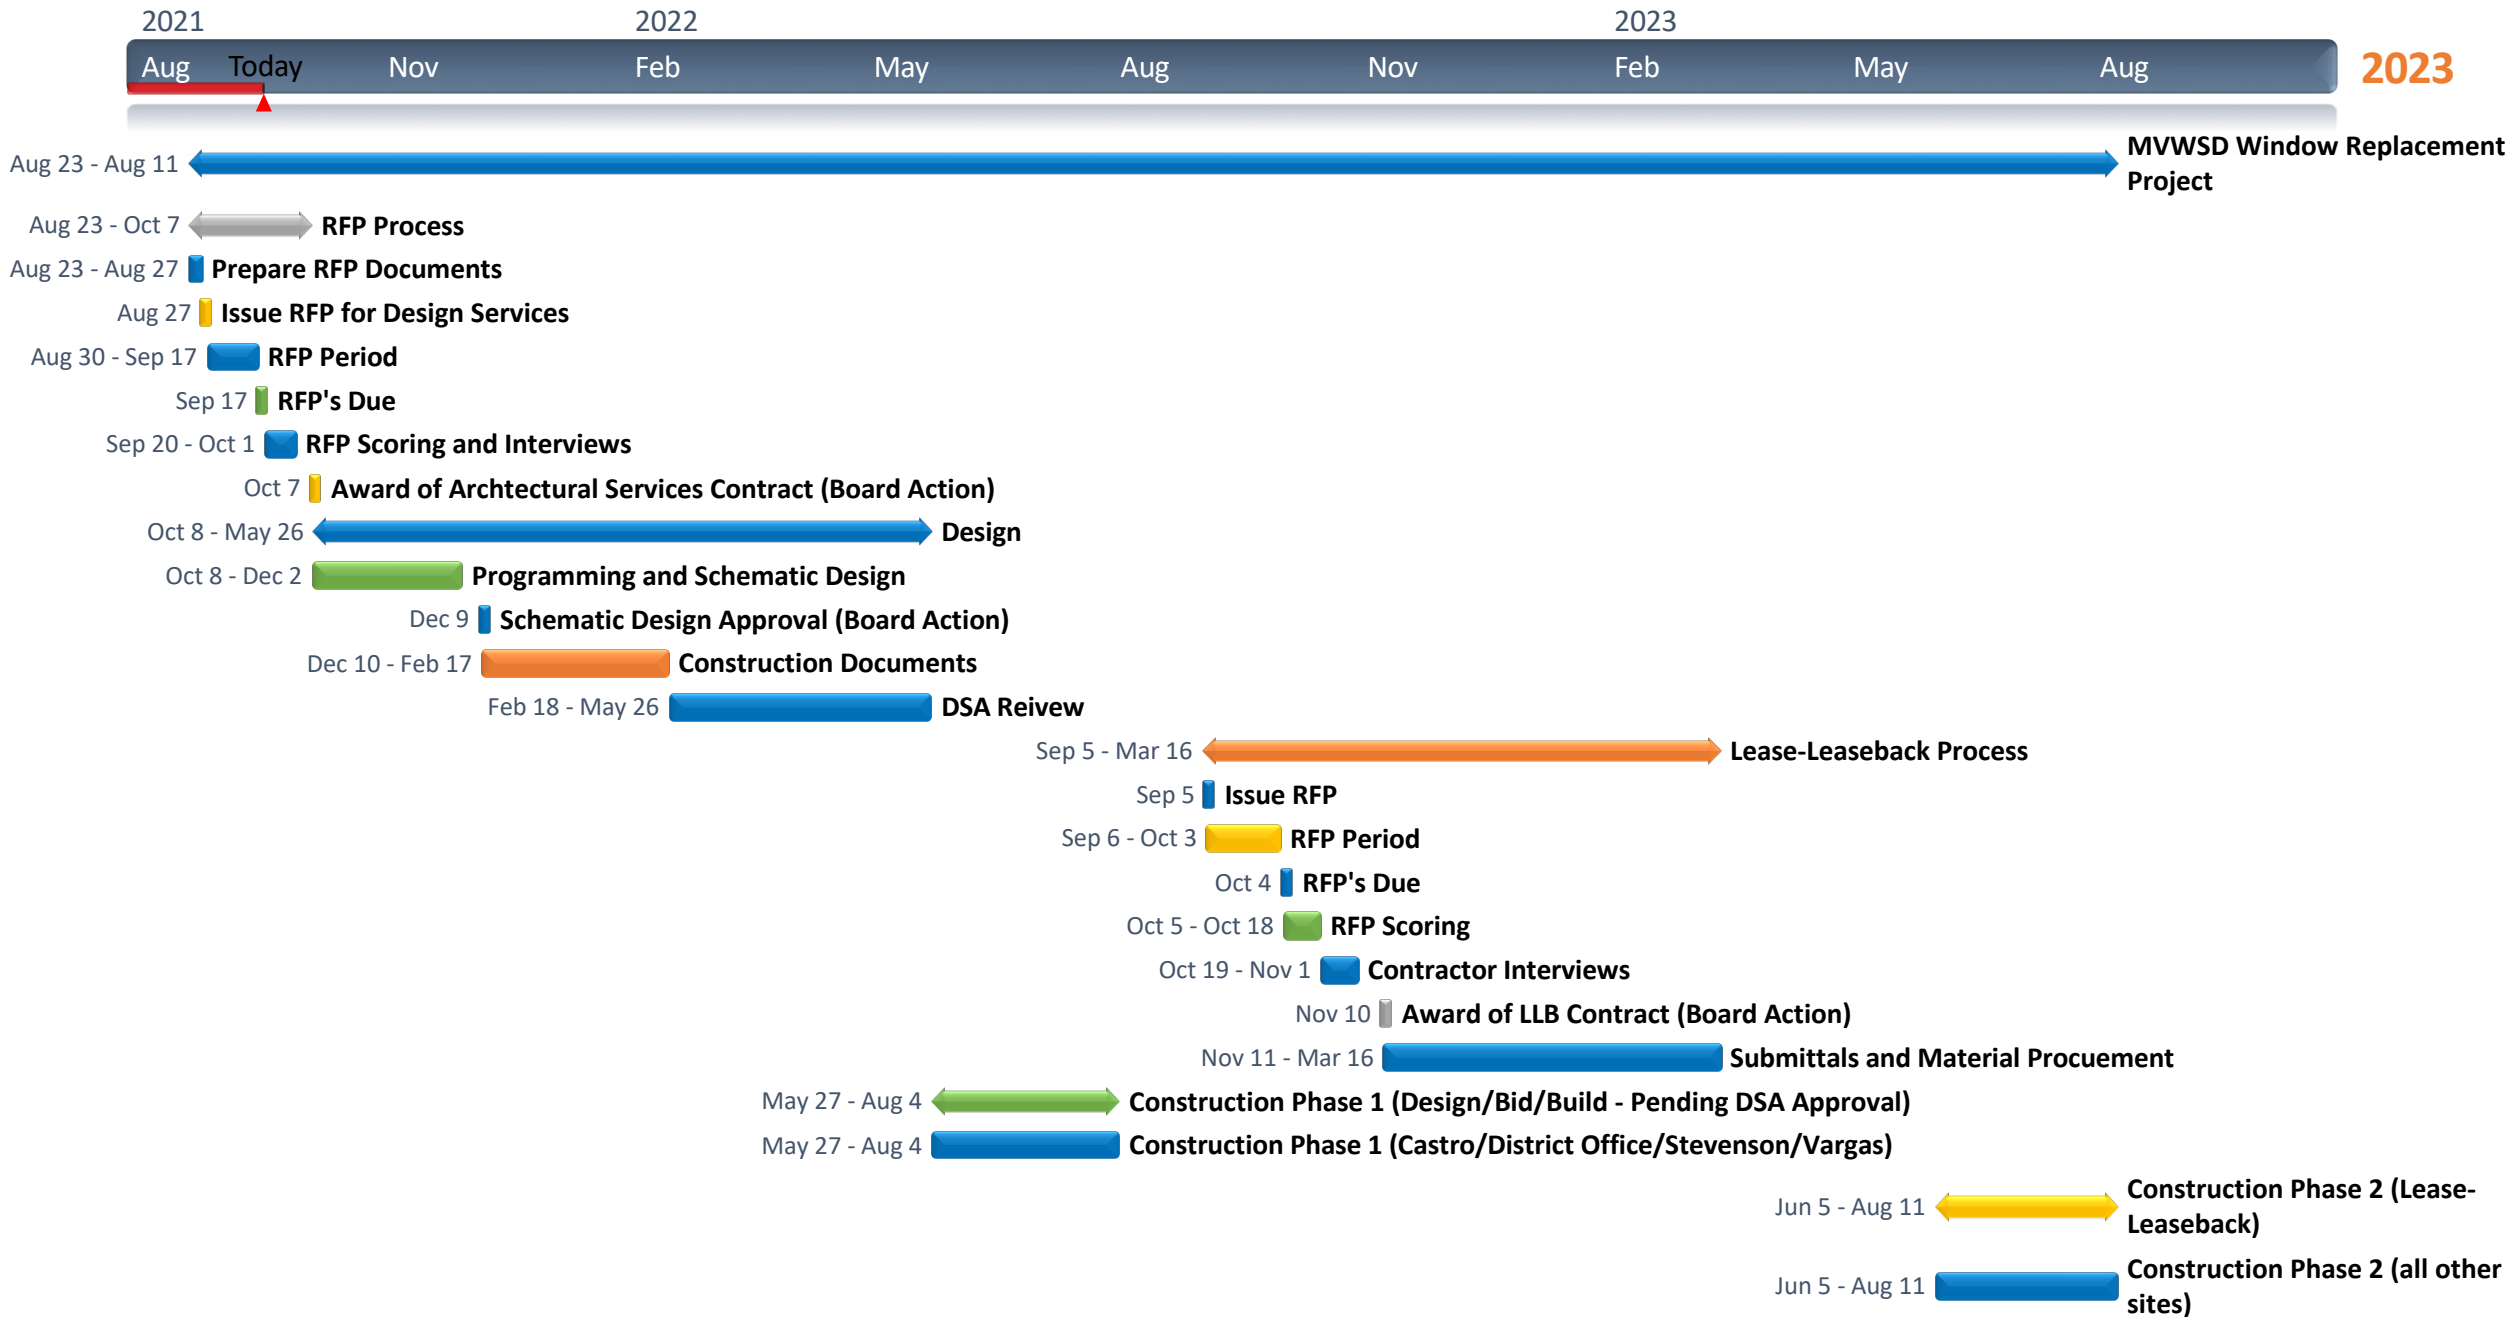

Community Restrooms at Castro/Mistral, Huff & Landels ES



Nov 16 - Mar 10 ← **Community Restrooms at Castro/Mistral, Huff and Landels ES**

Nov 16 - Feb 26 **Schematic Design**

Mar 1 - May 21 **Review Process with District stakeholders and City**

Jun 3 **BOT Info - SD Approval**

Jun 17 **BOT Action SD Approval**

Jun 18 - Oct 7 **Construction Documents**


Jun 18 - Oct 21 **Award and Procure Manufactured Restroom Buildings**

Oct 8 - Nov 18 **DSA Review (Access Only)**


Nov 19 - Dec 23 **Bid & Award Site Package**

Dec 24 - Mar 10 **Construction**


Surveillance Cameras

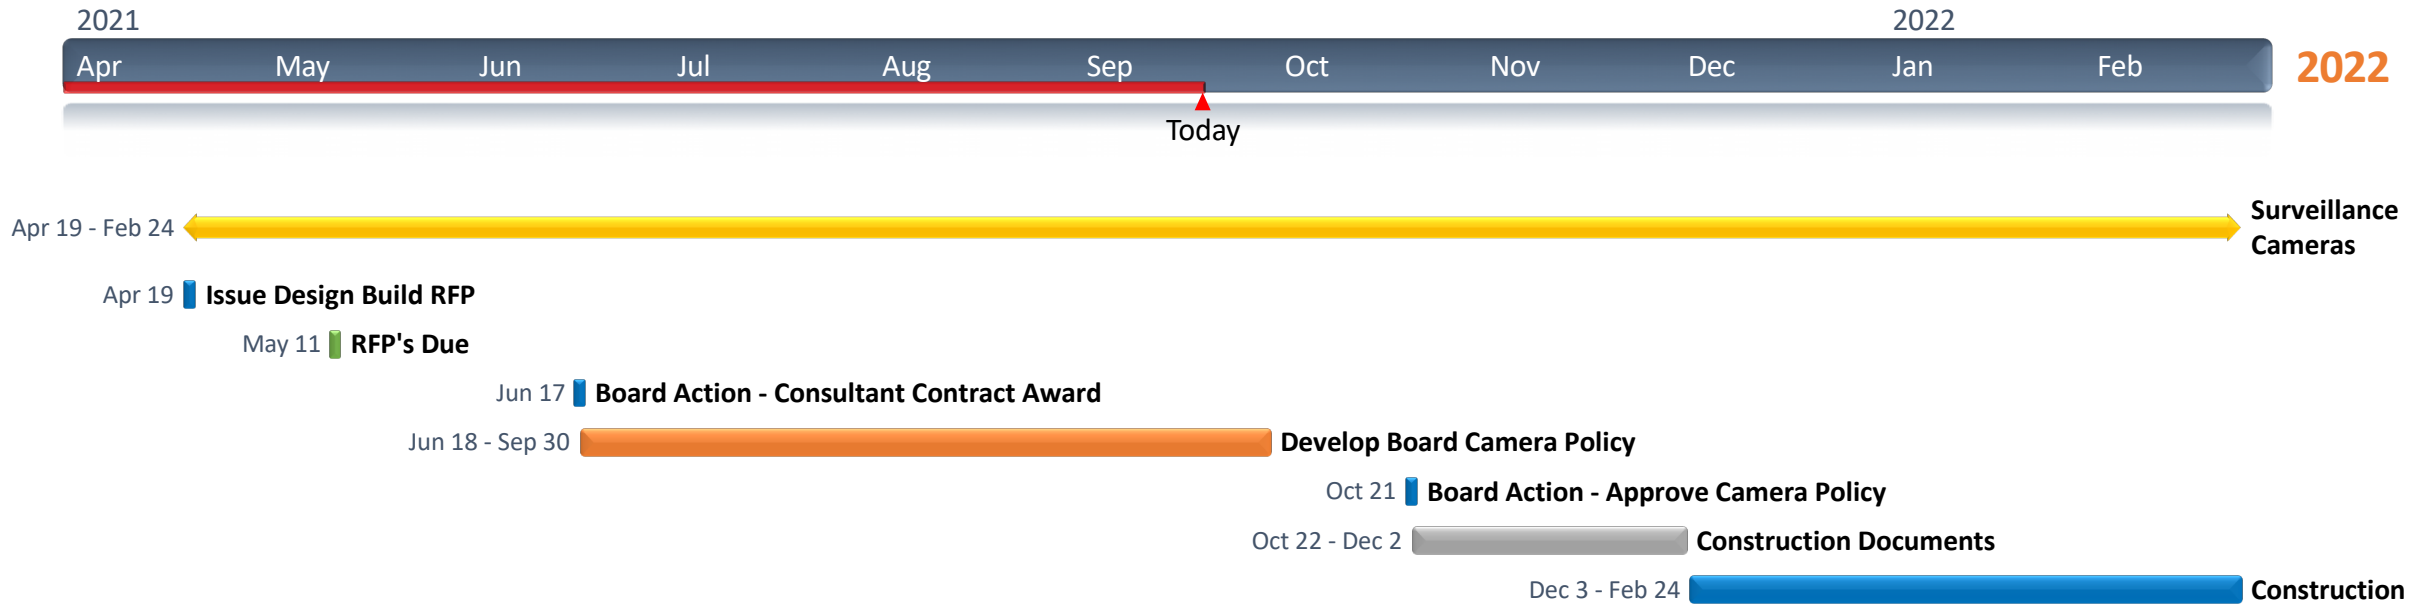

Vargas Carport (Full DSA Review)

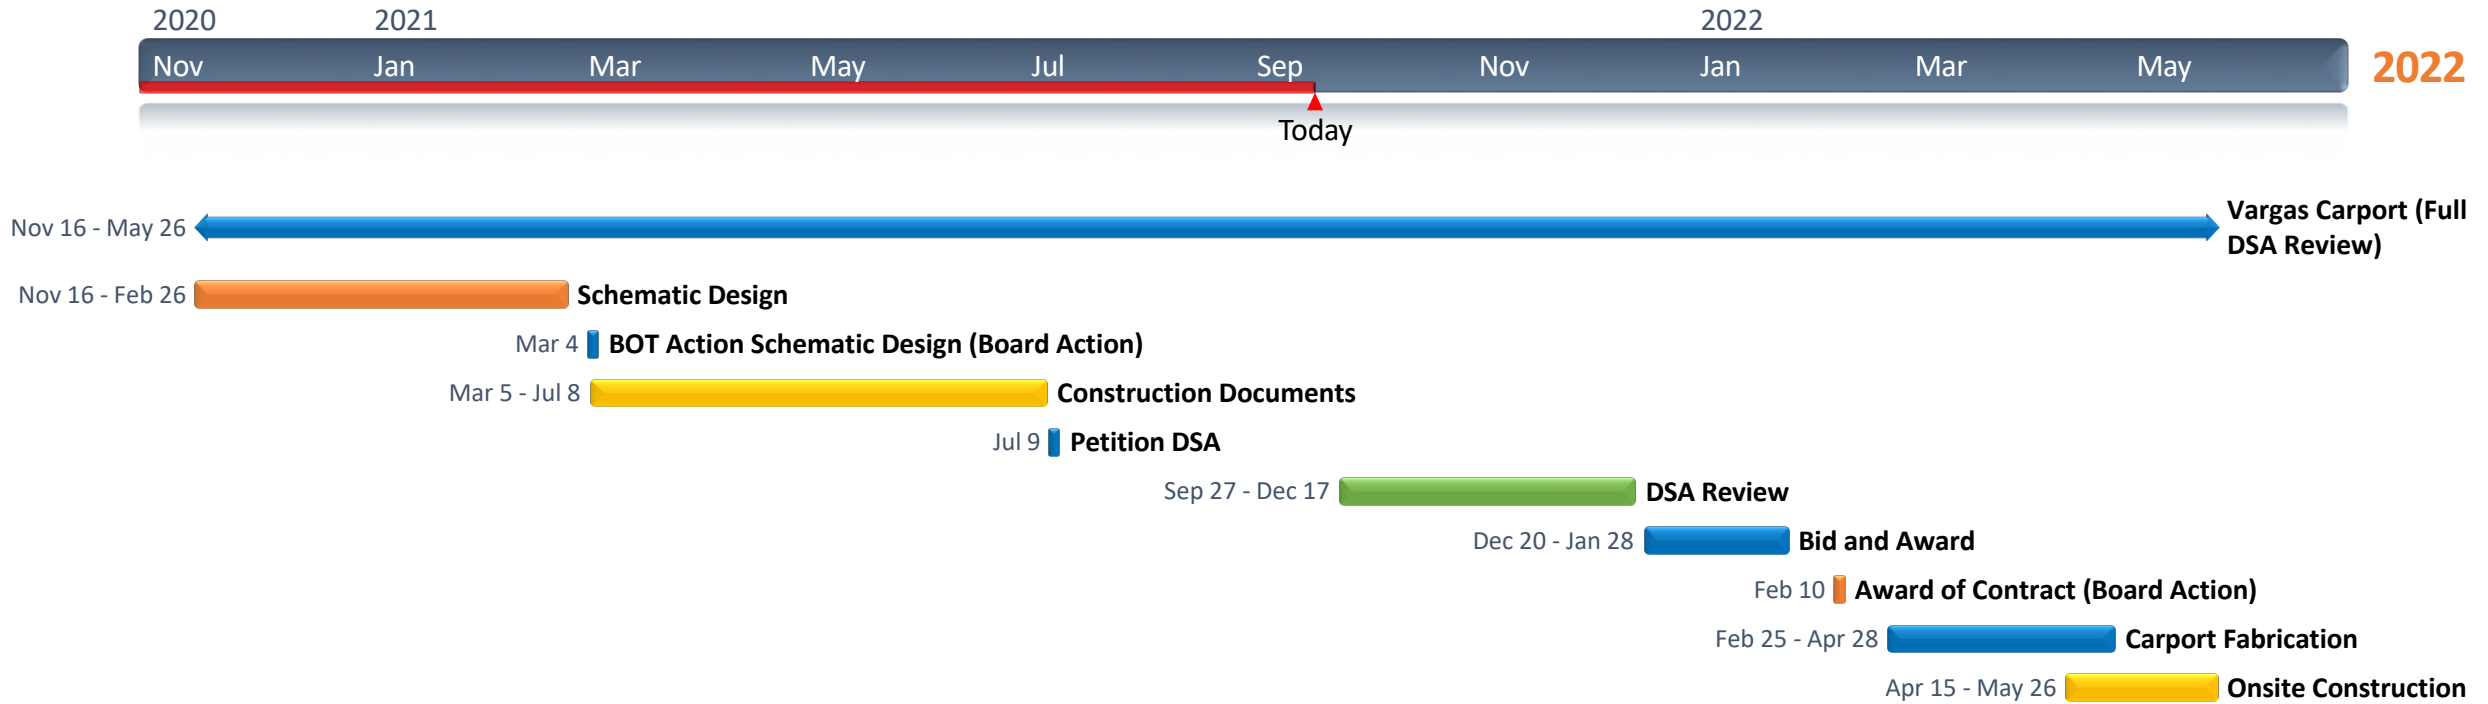

Paving Project- Phase 2 at Bubb, Imai & Crittenden (PENDING BOARD APPROVAL)

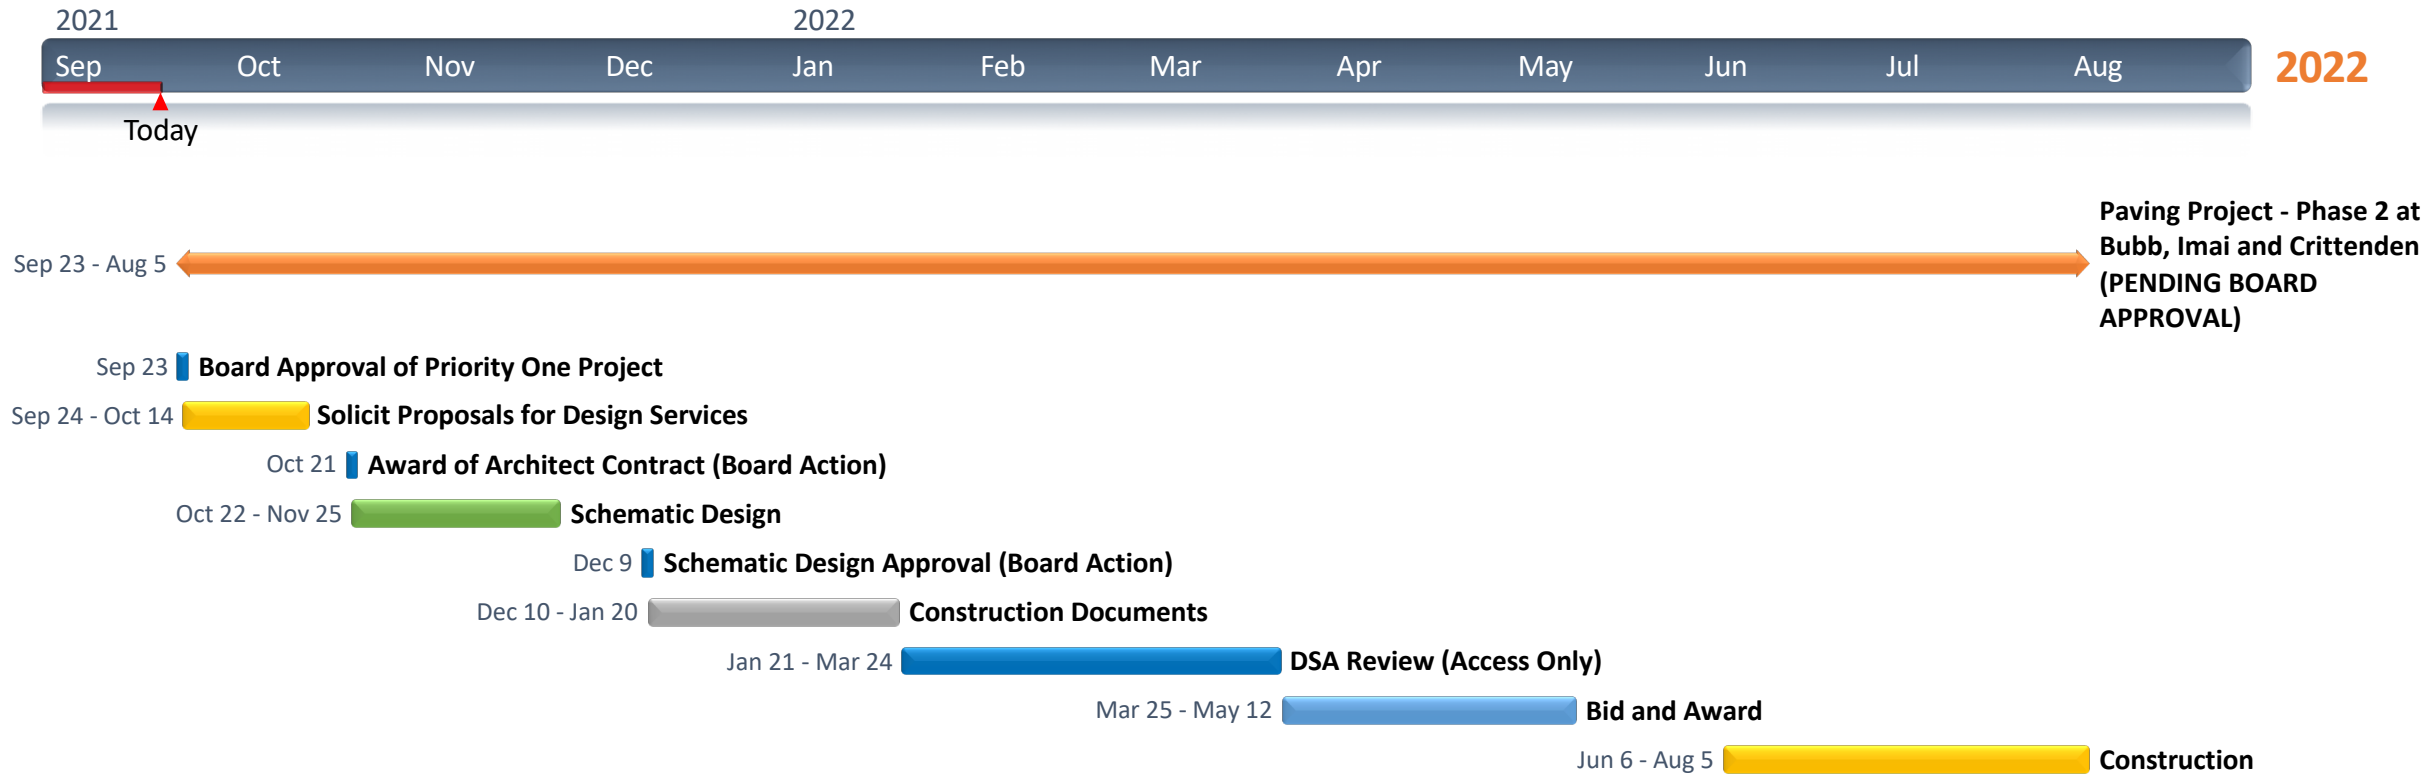

MUR Roll Up Doors- Stevenson/Vargas (PENDING BOARD APPROVAL)

